M. A. R. 57 (Rule 116)
Measurement Book

No. B 490323

Serial No. 1st and final Bill

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency ..... K. Jagadish Contractor.

Date of commencement of work ..... D.O. Recorded: 10-08-2018

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of Works :-	Providing C.C. Camera at Garbage Block spots in Ward No 12, Shettyhalli sub-Division.					
	Estimated Cost Rs.	10.00 Lakhs					
	DOB. No =	012-17-000054, P-Code. 3110					
	Work order No =	EE/DD/WO/104/2017-18 - Dt. 06-12-2017.					
	① Providing of Hikvision 8 channel NVR/DVR/DS 7608 N2-E1						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	CNVR. default Unstamped Hard Copy Rate Complete as per the directions of Engineers-in-Charge of the Work.						
	a) K.G. Hollymar Kodanda Rama Temple	1 No	-	-	-	1 No	
	b) Y-Mand-Circle	1 No	-	-	-	1 No	
	c) Laxmi Temple Abbigere	1 No	-	-	-	1 No	
	d) AE Sched, K.G. Holly	1 No	-	-	-	1 No	
	e) Abbigere Circle	1 No	-	-	-	1 No	
	f) Laxmipura Road near Swagatha Main Road Junction	1 No	-	-	-	1 No	
						6 Nos @ 16310.18/Each	97861.41

M. A. R. 57 (Rule 116)
Measurement Book

No. B 490324

rial No. .....
ime of Work ..... From..... To.....
ime of Contractor of nature of Agency .....
ite of commencement of work .....

ate	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
2)	Supplying of Hikvision PTZ Camera DS-2DE-7174-A with Pole mount and power supply (Data Rate) complete as per the directions of Engineers-in-charge of the work.						
		6 Nos	-	-	-	6 Nos @ 62216.62/Each	3,73,299.72
3)	Supplying of 27 B Hand-Drill-set at (Data Rate) Complete as per the directions of Engineers-in-Charge of Work.						
		6 Nos @ 7634.55/Each				Rs	45807.30

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	4) Supplying of C post PCC with TP Links (Data Rate) complete as per the directions Engineer-in-charge of work.						
		6 Nos	-	-	-	6 Nos @ 2478.75/Each	14872.50
	5) Supplying of 4 pin spike pcc. Conc. Reputed (data Rate) complete as per the directions Engineer-in-charge of work.						
		6 Nos	-	-	-	6 Nos @ 347.02/Each	2082.12
	6) Supplying of outdoor supportable CA & CA Cable (Data Rate) Complete as per specifications & drawings						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 490325

...ial No. .....
...me of Work Asphalting ~~and~~ Improvements ..... From..... To.....
...me of Contractor of nature of Agency .....
...te of commencement of work .....

...ate	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	Engineer-in-charge of work.						
	~~1 at 165~~						
	a)	1	165.00	-	-	165.00	with
	b)	1	168.00	-	-	168.00	
	c)	1	170.00	-	-	170.00	
	d)	1	164.00	-	-	164.00	
	e)	1	166.00	-	-	166.00	
	f)	1	162.00	-	-	162.00	
						995.00 sqm	
						@ 138.81/sqm	138115.95

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	fabricating, supplying and erecting designed tabular poles hr. mtr heavy duty three sections and provided 2 coats of Red oxide paint and finished with 2 coats of enamelled painting approved quality and colour and M.S. base plate of suitable size welded at the bottom of the pole (as per 2527) and 4 nos dia GI/flexible pipe pipes... mtr length to be fixed in heavy gauge polycarbonate control box including 5 way connector of size 167 × 125 × 82 mm for 7.5 mtr pole (200 mm box 90 mm for necessary length of pole with front opening cover, with locking arrangement and suitable capacity. MCB/DP						

M. A. R. 57 (Rule 116)
Measurement Book

No. B

490326

Material No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	district. The pole shall be erected on C.C. (1:2:4) including excavation and refilling, planting depth of the pole to the GL and the coping C.C. shall be upto 0.6 mtr above GL as per IS 2713.1.1. Erecting light duty pole on foot path @ 7.5 mtr (4.5 mtr Ht. 114.3 mm dia 4 mm thick & 1.50 mtr Ht 88.9 mm dia, 4 mm thick & 1.50 Ht, 76.1 mm dia 3.25 mm thick) as per IS-410 89-5 (Base plate of size 300 × 300 × 6 mm) complete as per the directions Engineer-in-charge						

Scanned by CamScanner

MEASUREMENT BOOK

M. A. R. 57 (Rule 116)
Measurement Book

No. B 490327

rial No. .....
me of Work ..... From..... To.....
me of Contractor of nature of Agency .....
te of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	of the work	6Nos	-	-	-	6Nos, @ 8923.50/-	53541.00
8)	Supplying and fixing of monitor fan complete. Make Almonard / LG / Philips / Videocon (Date Rate) Complete as per the direction of Engineer-in-Charge of the work.						
		6Nos	-	-	-	6Nos @ 9915.00/-	59490.00
9)	Outdoor Suppriable type CFL Cabling, Laying Changes (Date Rate) Complete as per the direction Engineer-in-Charge of the work						

ate	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
		9 No. on pr. Nos. (1) = 995 wts Additional Cable = 105 1100 wts					
10)	Fabricating, Supplying and mounting MS Box made out of SS. Sheet @ 138.91/- Kg. Suitable for Floor / Wall mounting, fully weather proof with provision for better heat dissipation, provided with hinged front cover, equipped with tamper proof locking arrangement, with suitable size CW Glands with necessary cable Entry pipe with gland and bar						152691.00

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	should be finished with 2 coats of Red oxide primer, paint and finally finished with approved colour enamel paint etc. Complete (b) 165 kg (plan Ele 2011-15, complete as per the direction of Engineer-in-charge of work.						
Chd = Rs 10/8/2018		1	10.00	154.00	= 154000.00	89.63	
						C 0.33 sqm	
						50820.00	
					Total R	98858.63	

10/08/2018

M. A. R. 57 (Rule 116)
Measurement Book

No. B 490328

rial No. .....
me of Work ..... From ..... To .....
me of Contractor of nature of Agency .....
te of commencement of work .....

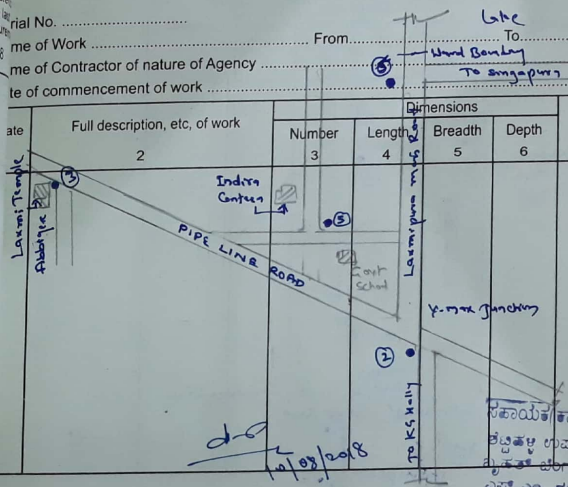

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
ate	2	3	4	5	6	7	8

10/08/2018

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಗ್ರೇಟರ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Scanned by CamScanner
